Appendix B · Scrum project management evidence

QuickVolunteer · CPU4106 Group Project · Three one-week sprints, 9-29 October 2026 · Source: the team's Scrum tracker (Excel), which is submitted with the GitHub artefact.

B1 · Product goal, team and sprint cadence

Product Goal. Help seekers and volunteers connect through clearly described 15–60 minute local or remote tasks. One individual account can ask for help, give help or both; administrators check optional ID verification, profile changes and concern reports.

Khadija Idbihi · Scrum Master

Facilitates Scrum events and removes impediments; leads research, requirements, ERD and normalisation, and testing.

Alexandra Nastase · UI/UX Lead

Personas, journeys, prototype, diagrams, front end and accessibility tools.


Gioacchino Rendine · Technical Lead

Flask API, MySQL, security and back-end tests.

Sprint	Dates	Sprint Goal	Review / Retrospective	Status
Sprint 1	09-15 Oct 2026	Research, analysis, prototype and MySQL/Flask design foundation.	Review and Retrospective 15 Oct	Done
Sprint 2	16-22 Oct 2026	Deliver the usable MVP website end-to-end using MySQL and a Python Flask API.	Review and Retrospective 22 Oct	Done
Sprint 3	23-29 Oct 2026	Enhance the MVP with skills-based suggestions, activity history (no hours), reviews, in app notifications, optional ID verification, member summaries, the accessibility tools bar, the admin menu and permissions, the location map and faster pages; test and prepare delivery.	Review and Retrospective 29 Oct	Done
Delivery	30 Oct-09 Nov 2026	Buffer 30 Oct; GitHub 02 Nov; viva Week 5; article and PPT 09 Nov	-	Done

Table B1. Sprint cadence. Each sprint has Sprint Planning, Daily Scrums, a Sprint Review and a separate Sprint Retrospective.

B2 · The sprint cycle

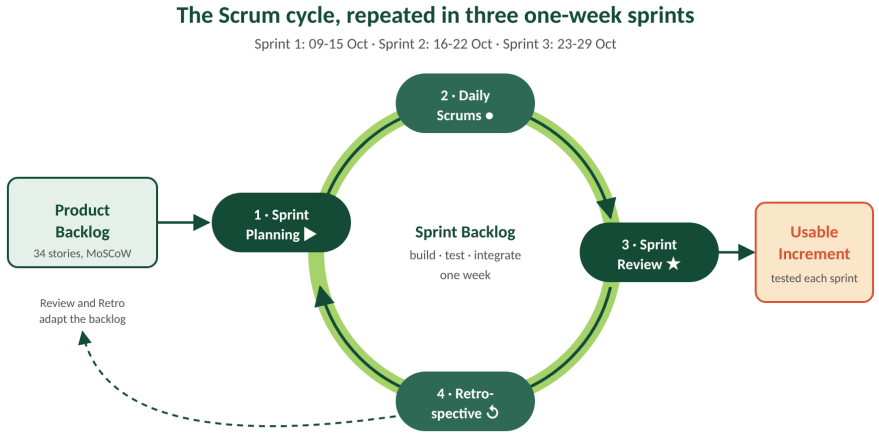

3
one-week sprints with 4 Scrum events each

24
meetings recorded with attendance and decisions (Section B6)

20 / 34
stories delivered; 13 kept for later, 1 merged

104
automated tests passing; 4 user testers

Figure B1. The Scrum cycle repeated in each one-week sprint: the Review and the Retrospective adapt the Product Backlog for the next sprint.

Scrum step	Sprint 1 · 09-15 Oct	Sprint 2 · 16-22 Oct	Sprint 3 · 23-29 Oct
Sprint Goal	Research, analysis, prototype and MySQL/Flask design foundation	Deliver the usable MVP website end to end with MySQL and a Python Flask API	Enhance the MVP: skills-based suggestions, activity history, reviews, notifications, safety, accessibility; validate
1 ▶ Sprint Planning	09 Oct (kick-off): product goal, roles, SDG and initial scope agreed	16 Oct: MVP stories selected (US-01 to US-12, US-16)	23 Oct: feature and improvement stories selected; team decisions recorded
Sprint Backlog	S1-01 to S1-08: research, personas, requirements, diagrams, ERD, Flask API and schema, prototype review	S2-01 to S2-09: accounts, posting, search, offers, accept/decline, completion, admin checks, onboarding, integration	S3-01 to S3-20: live API connection, verification, notifications, member summary, matching, history, reviews, accessibility, admin menu, location, speed, testing
2 ● Daily Scrums	12, 13, 14, 15 Oct	16, 19, 20, 21, 22 Oct	23, 26, 27, 28, 29 Oct
Testing in the sprint	Prototype review with 4 testers (Khadija, Gioacchino, Sohel, Chaymaa): 4 findings	Database tests (19 Oct): 11 design tests, 5 problems found and fixed in the design	104 automated tests passing; live-site testing with the same 4 testers: 3 findings, 3 changes
Usable Increment	Research evidence, personas and journeys, CASE diagrams, ERD in 3NF, Flask API and MySQL schema, Figma prototype	Working MVP: sign up, post, find, offer, accept, both confirm, admin checks	Enhanced, tested website live on Render with MySQL on Aiven

Scrum step	Sprint 1 · 09-15 Oct	Sprint 2 · 16-22 Oct	Sprint 3 · 23-29 Oct
3 ★ Sprint Review	15 Oct · Increment: research evidence, personas and journeys, normalised ERD, CASE diagrams, Flask API and MySQL schema, Figma prototype. Feedback (4 testers: Khadija, Gioacchino, Sohel, Chaymaa): • people often both ask for and offer help • organisations and donations were broader than the micro-volunteering idea • some elements had low contrast Backlog changes for Sprint 2: • scope cut to individuals only; organisations, campaigns and donations moved to Later (US-30, US-33) • one shared account to ask and to help (US-03 merged into US-01) • administrator role added to keep the platform safe • contrast improved in the prototype • Sprint 2 Goal: a usable MVP working end to end on MySQL and Flask	22 Oct · Increment: working MVP (sign up, post, find, offer, accept, both confirm, admin checks). Feedback: • help seekers wanted to know who is coming before accepting • the database tests showed that the design needed stronger rules Backlog changes for Sprint 3: • optional ID verification (US-11) • in-app notifications for both sides (US-21) • member summary before choosing (US-22) • activity history without hours (US-14) • accessibility tools moved from Later into Sprint 3 (US-19) • accounts active from sign-up; admins can hide reviews; each report names one target • DBS checks kept out of this version (US-17)	29 Oct · Increment: enhanced, tested website live on Render, in four main areas: • Accessibility (US-19): tools bar on all 23 pages, keyboard access and skip link • Map and location: postcode only, area name worked out automatically; location panel with a map, Locate me and a distance filter • Admin access (US-28): own menu and dashboard; check ID documents, review reports, hide reviews, suspend members, delete a request • Responsive design: every page checked at 10 screen sizes, from 320 to 1920 px Feedback: live-site testing with 4 users led to 3 changes (clearer task status, Verified badge in the member summary, report link on the task page). Release decision: approved for the GitHub submission on 2 Nov.
4 ↻ Sprint Retrospective	Went well: Mutual trust from previous projects meant roles and the project idea were agreed quickly. The Gantt chart and milestones were set up immediately. The prototype was tested with four people (two external), and the Sprint Review led to a clear scope decision. To improve: Splitting work only by strengths risked overloading one person. Working in parallel produced inconsistent documents, and the first database design was too large for our time. Action: Each work item gets a coordinator and a helper, with members supporting each other every week. Key shared decisions are agreed at Sprint Planning before parallel work starts, and the Scrum Master checks all documents against each other before each Review.	Went well: The MVP worked end to end: sign up, post, find, offer, accept and both confirm. Bringing our first DFD draft to the CASE tools session showed straight away what was missing, so we corrected it to the tutor's requirements. The database tests found 5 design problems early, before they reached the website. We compared Flask and FastAPI with research and made a reasoned decision to keep Flask. To improve: We drew the DFDs before the lecture with incomplete knowledge, so they needed rework. The back-end technology was questioned mid-project, which cost time and could have meant rebuilding everything. Action: Compare the main technologies during planning, before building. Bring draft diagrams to sessions to get early feedback. Keep testing the database design before building features on it.	Went well: Having learnt from the previous sprints, the Scrum Master anticipated the questions and problems before each meeting. In this crucial phase of the project the Scrum Master supported the team with clear ideas, clear decisions and clear communication, so everyone knew how to proceed, and trusted each member with their work. Every idea was listened to and checked for feasibility. The four Sprint 3 areas were delivered, and testing became structured: recorded test cases, automated tests and live-site testing with four users, which led to three changes. To improve: Website testing found changes that affected the database, so the ERD had to be updated late in the sprint. Documents, diagrams and test numbers drifted from the built system and needed an alignment review at the end. Action (for future projects): Prepare each meeting with a short list of expected issues and possible solutions. Test with users earlier, so database changes happen before features are built on them. Keep one source of truth and update diagrams and documents in the same sprint as the code.
Adapt → next sprint	Sprint 2 backlog built around one account, individuals only, admin role	Sprint 3 decisions (23 Oct): optional verification, in-app notifications, no hours, accessibility tools moved from Later into Sprint 3	Release: README, GitHub artefact 02 Nov, viva rehearsal, article and PPT 09 Nov

Table B2. How each sprint inspected and adapted the product. The 'Adapt → next sprint' row shows how each Review and Retrospective changed the following sprint.

B3 · Product Backlog (MoSCoW)

34 user stories prioritised with MoSCoW [Agile Business Consortium]: **Must** 11 **Should** 5 **Could** 4 **Won't (this time)** 13 **Merged** 1 . Full user stories and acceptance criteria are in the tracker.

ID	Item	MoSCoW	Release / Sprint	Status	Persona	Lead / collaborator
US-01	Create account and log in	**Must**	Sprint 2 MVP	Done	Adam, Sophie, Nadia, Daniel	Gioacchino (API) + Alexandra (UI)
US-02	Profile, skills and preferences	**Must**	Sprint 2 MVP + Sprint 3	Done	Adam, Sophie, Nadia	Alexandra + Gioacchino
US-03	Help seeker profile (merged)	**Merged**	Merged	Merged	—	Team
US-04	Post a help task	**Must**	Sprint 2 MVP + Sprint 3	Done	Nadia	Gioacchino (API/DB) + Alexandra (UI)
US-05	Search and filter tasks	**Must**	Sprint 2 MVP + Sprint 3	Done	Adam, Sophie	Whole team
US-06	View a task and offer help	**Must**	Sprint 2 MVP + Sprint 3	Done	Adam, Sophie	Gioacchino + Alexandra
US-07	Accept or decline an offer	**Must**	Sprint 2 MVP + Sprint 3	Done	Nadia	Gioacchino + Alexandra
US-08	My tasks (volunteer)	**Should**	Sprint 2 MVP + Sprint 3	Done	Adam, Sophie	Alexandra + Gioacchino
US-09	My requests (help seeker)	**Should**	Sprint 2 MVP	Done	Nadia	Alexandra + Gioacchino
US-10	Confirm task completed	**Must**	Sprint 2 MVP + Sprint 3	Done	Adam, Sophie, Nadia	Gioacchino + Alexandra
US-11	Optional ID verification	**Must**	Sprint 2 MVP + Sprint 3	Done	Nadia, Adam, Sophie, Daniel	Gioacchino (API) + Alexandra (UI) + Khadija (requirements)
US-12	Report a concern and admin review	**Must**	Sprint 2 MVP + Sprint 3	Done	Nadia, Adam, Sophie, Daniel	Gioacchino + Alexandra + Khadija
US-13	Tasks matched to my skills	**Could**	Sprint 3	Done	Adam, Sophie	Gioacchino + Alexandra
US-14	Activity history	**Could**	Sprint 3	Done	Adam, Sophie, Nadia, Daniel	Khadija + Alexandra
US-15	Leave a review after a task	**Could**	Sprint 3	Done	Nadia, Adam, Sophie	Gioacchino + Alexandra
US-16	Onboarding: area, ask or give help, skills	**Could**	Sprint 2 MVP + Sprint 3	Done	Adam, Sophie, Nadia	Khadija + Alexandra
US-17	DBS checks	**Won't (this time)**	Later	Later	Sophie, Daniel	Team
US-18	Messages	**Won't (this time)**	Later	Later	Nadia, Sophie	Team
US-19	Accessibility tools bar	**Should**	Sprint 3	Done	Nadia, Adam, Sophie, Daniel	Alexandra
US-20	Change language	**Won't (this time)**	Later	Later	All members	Team

ID	Item	MoSCoW	Release / Sprint	Status	Persona	Lead / collaborator
US-21	In app notifications	**Must**	Sprint 3	Done	Adam, Sophie, Nadia, Daniel	Gioacchino + Alexandra
US-22	Member summary before choosing	**Must**	Sprint 3	Done	Adam, Sophie, Nadia	Alexandra + Khadija
US-23	Email or text notifications	**Won't (this time)**	Later	Later	Adam, Sophie, Nadia	Team
US-24	Profile photo	**Won't (this time)**	Later	Later	Adam, Sophie, Nadia	Team
US-25	Preferred connections	**Won't (this time)**	Later	Later	Nadia, Adam, Sophie	Team
US-26	Volunteer levels	**Won't (this time)**	Later	Later	Adam, Sophie, Daniel	Team
US-27	Choose extra details to share	**Won't (this time)**	Later	Later	Adam, Sophie, Nadia	Team
US-28	Admin menu and permissions	**Should**	Sprint 3	Done	Daniel	Alexandra + Khadija
US-29	Faster pages	**Should**	Sprint 3	Done	All members	Alexandra
US-30	Organisations and associations	**Won't (this time)**	Later	Later	Daniel	Team
US-31	Group volunteering	**Won't (this time)**	Later	Later	Adam, Sophie	Team
US-32	Community events	**Won't (this time)**	Later	Later	Adam, Sophie, Nadia	Team
US-33	Donations	**Won't (this time)**	Later	Later	All members	Team
US-34	Mobile app	**Won't (this time)**	Later	Later	All members	Team

Table B3. Product Backlog ordered by ID. Earlier labels were unified to MoSCoW: Medium → Could, Low → Won't (this time).

B4 · Sprint Plan

SPRINT 1 · 09–15 OCT · GOAL: RESEARCH/DESIGN FOUNDATION; BASELINE PROTOTYPE AND DATABASE ARCHITECTURE

Work ID	Linked stories	Work item / outcome	Coordinator	Helper	Status	Evidence / Definition of Done
S1-01	-	Kickoff, agree project goal, SDG challenge and team ways of working	Khadija	Gioacchino + Alexandra	Done	Meeting record; project brief
S1-02	-	Research user needs, questionnaire and competitor/context analysis	Khadija	Alexandra	Done	Research notes, survey evidence and sources
S1-03	-	Create personas and user journey; validate with team	Khadija	Alexandra	Done	Personas and user journey aligned to target users
S1-04	-	Define requirements, project boundary, user stories and priority	Khadija	Team	Done	Scope decisions: no donations, organizations or campaigns; Admin added
S1-05a	-	Create the user flow, use case diagram and data flow diagrams (level 0 and 1)	Alexandra	-	Done	Figma user flow; use case and DFDs in draw.io
S1-05b	-	Normalise the data (UNF to 3NF) and design the ERD	Khadija	-	Done	Normalisation workbook (Excel) and ERD (draw.io)
S1-05c	-	Design the three-tier system architecture	Gioacchino	-	Done	System architecture diagram (draw.io)
S1-06	-	Set up Flask API and MySQL schema aligned to approved ERD	Gioacchino	-	Done	Flask API and MySQL schema built (15 tables in Sprint 3); schema loads from database/schema.sql
S1-07	-	Prototype review and design decisions; record accepted/rejected choices	Alexandra	Khadija	Done	Figma prototype and decision notes
S1-08	-	Sprint Review and Sprint Retrospective; capture outcomes separately	Khadija	Team	Done	Actual attendance, feedback, decisions and improvement actions

Table B4. Sprint 1 backlog: work items, coordinators and evidence.

SPRINT 2 · 16–22 OCT · GOAL: MVP WEBSITE WORKING END-TO-END ON MYSQL + FLASK API

Work ID	Linked stories	Work item / outcome	Coordinator	Helper	Status	Evidence / Definition of Done
S2-01	US-01, US-02	Build and integrate registration/login and unified user profile	Gioacchino + Alexandra	-	Done	Register, log in, log out and shared profile work end to end; back end tests and live browser checks pass
S2-02	US-04	Create task posting form and persist task data	Alexandra + Gioacchino	-	Done	Tasks saved in MySQL with 15 to 60 minutes, deadline, in person or remote; checked in the browser and in Flask

Work ID	Linked stories	Work item / outcome	Coordinator	Helper	Status	Evidence / Definition of Done
S2-03	US-05, US-06	Browse/filter tasks, view details and submit an application	Alexandra + Gioacchino	-	Done	Find a task lists open tasks with filters; task page; one offer per volunteer; tested
S2-04	US-07, US-08, US-09	Handle accept/decline and personal task/application views	Gioacchino + Alexandra	-	Done	Accept or decline with status checks; My tasks and My requests show only the member's own items; tested
S2-05	US-10	Complete task workflow	Team	-	Done	Both people confirm; task becomes Completed; tested
S2-06	US-11, US-12	Admin verification and concern report/moderation flow	Alexandra	Khadija	Done	Admin page: verifications and concern reports, admin only; tested
S2-07	US-01–US-12, US-16	Integrate routes/pages/API/database and run acceptance checks continuously	Team	-	Done	Website connected to the Flask API (live mode) and checked end to end
S2-08	US-16	Add onboarding for area, ask/give/both preference and skills (at least one to finish)	Alexandra	Khadija	Done	Onboarding saves area, ask or give help or both and skills; skip path works
S2-09	-	Sprint Review and Sprint Retrospective (separate events)	Khadija	Team	Done	Review increment and adapt backlog; retro creates improvement actions

Table B5. Sprint 2 backlog: work items, coordinators and evidence.

SPRINT 3 · 23–29 OCT · GOAL: ENHANCE MVP WITH MATCHED TASKS, ACTIVITY HISTORY, REVIEWS AND QUALITY IMPROVEMENTS

Work ID	Linked stories	Work item / outcome	Coordinator	Helper	Status	Evidence / Definition of Done
S3-01	-	Agree Sprint 3 Goal; estimate/select feasible stories and improvement work	Team	-	Done	Team decisions recorded 23 Oct (verification, notifications, no hours, member summary, no editing of posted requests)
S3-02	US-19	Improve accessibility: accessibility tools bar on every page (US-19), skip to main content link, keyboard navigation, labels, focus, contrast and error messages	Alexandra	Khadija	Done	Tools bar built and checked on all 23 pages at desktop and phone size; before/after screenshots; remaining checklist items to finish
S3-03	-	Verify mobile responsiveness and fix priority layout issues	Alexandra + Gioacchino	-	Done	Every page checked at 10 sizes from 320 to 1920px with no sideways scrolling (25 Oct); team to check on real phones
S3-04	US-01–US-29	Run functional, integration, usability and end-to-end checks; fix priority defects	Khadija	-	Done	104 unique automated tests (418 assertions) pass against a separate test database (unittest reports 320 runs because three modules re-run the 72 core tests); 20 defects found and fixed in Sprint 3.

Work ID	Linked stories	Work item / outcome	Coordinator	Helper	Status	Evidence / Definition of Done
S3-05	-	Prepare README, architecture/setup notes, presentation and live demo rehearsal	Khadija	Alexandra + Gioacchino	Done	README for tutors (logins, what each user can do, tour), setup guides and testing and improvement document written; slides and rehearsal to do; 15–18 slides, 15-minute talk + 5-minute Q&A
S3-06	-	Sprint Review and Sprint Retrospective (separate events); finalize release evidence	Khadija	-	Done	Increment and feedback reviewed; improvement actions recorded; delivery ready
S3-07	US-13	Suggest tasks by skills first, then distance (postcode districts)	Team	-	Done	Suggestions follow the agreed rules; area hidden when there is no skill or location
S3-08	US-14	Show completed task history for both members (no hours); completed count for administrators	Alexandra + Khadija	-	Done	History is private to the member; a task is counted once; hours removed
S3-09	US-15	Allow participants to review after task completion; admin can hide or restore	Alexandra + Gioacchino	-	Done	One review each per completed task; moderation tested
S3-10	US-01–US-16	Connect the website to the Flask API (live mode) and keep the prototype mode for GitHub Pages	Team	-	Done	Pages use the API when Flask runs; prototype mode otherwise; CONNECTING_FRONTEND.md
S3-11	US-11	Optional ID verification: upload, private storage, admin check, delete after decision, verified badge and filter	Team	-	Done	Upload and admin tests pass; document deleted after the decision
S3-12	US-21	In app notifications both ways, and to administrators	Gioacchino + Alexandra	Khadija	Done	Notification tests pass; bell shows unread
S3-13	US-22, US-06, US-07	Member summary before offering or accepting; withdraw an offer	Khadija + Alexandra	-	Done	Summary shows only agreed fields; withdraw notifies the help seeker; tested
S3-14	US-02, US-12	Edit profile with admin check; reports about a member, task or something else with contact choice	Gioacchino + Alexandra	Khadija	Done	Admins notified of changes and reports; email shown only when contact is allowed; tested
S3-15	-	Align database and diagrams with the built system: schema (15 tables), ERD v3, normalisation v4, DFD, use case, architecture, persona journeys	Khadija	Alexandra	Done	Updated files in the Sprint 3 diagrams folder
S3-16	US-28	Admin menu and permissions: own menu, view only forms, delete a request, members search, sort and filters, admin profile	Alexandra + Khadija	-	Done	Delete route and test added; admin journey checked on phone and desktop
S3-17	US-02, US-04, US-05	Location: postcode only with area name; Choose a location panel with map, Locate me, Edit and suggestions	Alexandra	Gioacchino	Done	Checked on Find a task, Post a request, My profile and onboarding; neighbourhood field removed
S3-18	US-29	Faster pages: database connection pool, skills in the task list, parallel calls	Alexandra	Gioacchino	Done	Offer Support 15 to 5 API calls; all back end tests pass

Work ID	Linked stories	Work item / outcome	Coordinator	Helper	Status	Evidence / Definition of Done
S3-19	-	Website text and design: remove developer style text, Impact and About updates, Coming soon list, phone menu, 2027 demo dates	Alexandra + Khadija	-	Done	Changes from the team's change list checked at phone, tablet and desktop sizes
S3-20	US-08, US-12, US-22	User testing of the live site with 4 testers (Khadija, Gioacchino, Sohel, Chaymaa)	Khadija	-	Done	3 findings, 3 changes made (see User Testing sheet)

Table B6. Sprint 3 backlog: work items, coordinators and evidence.

DELIVERY · 30 OCT (INTERNAL) · GOAL: INTERNAL BUFFER / FINAL ARTEFACT READINESS CHECK

Work ID	Linked stories	Work item / outcome	Coordinator	Helper	Status	Evidence / Definition of Done
D-01	-	Confirm GitHub artefact, slides, article progress and Moodle deadlines	Team	-	Done	Internal review 30 Oct; lesson states GitHub artefact due 02 Nov and article/PPT Moodle submissions due 09 Nov; confirm exact details and viva slot

Table B7. Delivery backlog: work items, coordinators and evidence.

B5 · Gantt chart and Scrum events

Sprint 1 · Sprint 2 · Sprint 3 · Delivery · ◆ milestone · ▶ Sprint Planning · ● Daily Scrum · ★ Sprint Review · ↻ Sprint Retrospective

ID	Sprint	Task / Scrum event / milestone	Lead	Status	09 Oct	12 Oct	13 Oct	14 Oct	15 Oct	16 Oct	19 Oct	20 Oct	21 Oct	22 Oct	23 Oct	26 Oct	27 Oct	28 Oct	29 Oct	30 Oct	02 Nov	03 Nov	04 Nov	05 Nov	06 Nov	09 Nov
KEY MILESTONES & SUBMISSIONS																										
M-01	Milestone	**Project kickoff and team roles**	Team	Done	◆																					
M-02	Milestone	**Sprint 1 review: research, design and database foundation**	Team	Done					◆																	
M-03	Milestone	**Sprint 2 review: usable MVP increment**	Team	Done										◆												
M-04	Milestone	**Sprint 3 review: improvements and validation complete**	Team	Done															◆							
M-05	Internal	**Internal readiness check / buffer (30 Oct)**	Team	Done																◆						
M-06	Submission	**GitHub artefact submission deadline**	Team	Done																	◆					
M-07	Submission	**Academic article and group PPT Moodle deadline**	Team	Done																						◆
SPRINT 1 · GOAL: Research/design foundation; baseline prototype and database architecture																										
		Scrum events																								
	Sprint 1	Sprint Planning	Khadija (Scrum Master)	Done	▶																					
	Sprint 1	Daily Scrum	Whole team	Done		●	●	●	●																	
	Sprint 1	Sprint Review	Khadija (Scrum Master)	Done					★																	
	Sprint 1	Sprint Retrospective	Khadija (Scrum Master)	Done					↻																	
		Sprint Backlog work items																								
S1-01	Sprint 1	Kickoff, agree project goal, SDG challenge and team ways of working	Khadija + Gioacchino + Alexandra	Done																						
S1-02	Sprint 1	Research user needs, questionnaire and competitor/context analysis	Khadija + Alexandra	Done																						
S1-03	Sprint 1	Create personas and user journey; validate with team	Khadija + Alexandra	Done																						
S1-04	Sprint 1	Define requirements, project boundary, user stories and priority	Khadija + Team	Done																						
S1-05a	Sprint 1	Create the user flow, use case diagram and data flow diagrams (level 0 and 1)	Alexandra	Done																						
S1-05b	Sprint 1	Normalise the data (UNF to 3NF) and design the ERD	Khadija	Done																						
S1-05c	Sprint 1	Design the three-tier system architecture	Gioacchino	Done																						
S1-06	Sprint 1	Set up Flask API and MySQL schema aligned to approved ERD	Gioacchino	Done																						
S1-07	Sprint 1	Prototype review and design decisions; record accepted/rejected choices	Alexandra + Khadija	Done																						
S1-08	Sprint 1	Sprint Review and Sprint Retrospective; capture outcomes separately	Khadija + Team	Done																						
SPRINT 2 · GOAL: MVP website working end-to-end on MySQL + Flask API																										
		Scrum events																								
	Sprint 2	Sprint Planning	Khadija (Scrum Master)	Done						▶																

ID	Sprint	Task / Scrum event / milestone	Lead	Status	09 Oct	12 Oct	13 Oct	14 Oct	15 Oct	16 Oct	19 Oct	20 Oct	21 Oct	22 Oct	23 Oct	26 Oct	27 Oct	28 Oct	29 Oct	30 Oct	02 Nov	03 Nov	04 Nov	05 Nov	06 Nov	09 Nov
	Sprint 2	Daily Scrum	Whole team	Done						●	●	●	●	●												
	Sprint 2	Sprint Review	Khadija (Scrum Master)	Done										★												
	Sprint 2	Sprint Retrospective	Khadija (Scrum Master)	Done										↻												
		Sprint Backlog work items																								
S2-01	Sprint 2	Build and integrate registration/login and unified user profile	Gioacchino + Alexandra	Done						■	■	■														
S2-02	Sprint 2	Create task posting form and persist task data	Alexandra + Gioacchino	Done						■	■															
S2-03	Sprint 2	Browse/filter tasks, view details and submit an application	Alexandra + Gioacchino	Done							■	■														
S2-04	Sprint 2	Handle accept/decline and personal task/application views	Gioacchino + Alexandra	Done							■	■	■													
S2-05	Sprint 2	Complete task workflow	Team	Done								■	■													
S2-06	Sprint 2	Admin verification and concern report/moderation flow	Alexandra + Khadija	Done							■	■	■													
S2-07	Sprint 2	Integrate routes/pages/API/database and run acceptance checks continuously	Team	Done						■	■	■	■	■												
S2-08	Sprint 2	Add onboarding for area, ask/give/both preference and skills (at least one to finish)	Alexandra + Khadija	Done						■	■															
S2-09	Sprint 2	Sprint Review and Sprint Retrospective (separate events)	Khadija + Team	Done										■												
SPRINT 3 · GOAL: Enhance MVP with matched tasks, activity history, reviews and quality improvements																										
		Scrum events																								
	Sprint 3	Sprint Planning	Khadija (Scrum Master)	Done											▶											
	Sprint 3	Daily Scrum	Whole team	Done											●	●	●	●	●							
	Sprint 3	Sprint Review	Khadija (Scrum Master)	Done															★							
	Sprint 3	Sprint Retrospective	Khadija (Scrum Master)	Done															↻							
		Sprint Backlog work items																								
S3-01	Sprint 3	Agree Sprint 3 Goal; estimate/select feasible stories and improvement work	Team	Done											■											
S3-02	Sprint 3	Improve accessibility: accessibility tools bar on every page (US-19), skip to main content link, keyboard navigation, labels, focus, contrast and error messages	Alexandra + Khadija	Done											■	■	■									
S3-03	Sprint 3	Verify mobile responsiveness and fix priority layout issues	Alexandra + Gioacchino	Done											■	■	■	■								
S3-04	Sprint 3	Run functional, integration, usability and end-to-end checks; fix priority defects	Khadija	Done											■	■	■	■	■							
S3-05	Sprint 3	Prepare README, architecture/setup notes, presentation and live demo rehearsal	Khadija + Alexandra + Gioacchino	Done												■	■	■	■							
S3-06	Sprint 3	Sprint Review and Sprint Retrospective (separate events); finalize release evidence	Khadija	Done															■							
S3-07	Sprint 3	Suggest tasks by skills first, then distance (postcode districts)	Team	Done											■	■										
S3-08	Sprint 3	Show completed task history for both members (no hours); completed count for administrators	Alexandra + Khadija	Done											■	■										
S3-09	Sprint 3	Allow participants to review after task completion; admin can hide or restore	Alexandra + Gioacchino	Done											■	■										

ID	Sprint	Task / Scrum event / milestone	Lead	Status	09 Oct	12 Oct	13 Oct	14 Oct	15 Oct	16 Oct	19 Oct	20 Oct	21 Oct	22 Oct	23 Oct	26 Oct	27 Oct	28 Oct	29 Oct	30 Oct	02 Nov	03 Nov	04 Nov	05 Nov	06 Nov	09 Nov
S3-10	Sprint 3	Connect the website to the Flask API (live mode) and keep the prototype mode for GitHub Pages	Team	Done																						
S3-11	Sprint 3	Optional ID verification: upload, private storage, admin check, delete after decision, verified badge and filter	Team	Done																						
S3-12	Sprint 3	In app notifications both ways, and to administrators	Gioacchino + Alexandra + Khadija	Done																						
S3-13	Sprint 3	Member summary before offering or accepting; withdraw an offer	Khadija + Alexandra	Done																						
S3-14	Sprint 3	Edit profile with admin check; reports about a member, task or something else with contact choice	Gioacchino + Alexandra + Khadija	Done																						
S3-15	Sprint 3	Align database and diagrams with the built system: schema (15 tables), ERD v3, normalisation v4, DFD, use case, architecture, persona journeys	Khadija + Alexandra	Done																						
S3-16	Sprint 3	Admin menu and permissions: own menu, view only forms, delete a request, members search, sort and filters, admin profile	Alexandra + Khadija	Done																						
S3-17	Sprint 3	Location: postcode only with area name; Choose a location panel with map, Locate me, Edit and suggestions	Alexandra + Gioacchino	Done																						
S3-18	Sprint 3	Faster pages: database connection pool, skills in the task list, parallel calls	Alexandra + Gioacchino	Done																						
S3-19	Sprint 3	Website text and design: remove developer style text, Impact and About updates, Coming soon list, phone menu, 2027 demo dates	Alexandra + Khadija	Done																						
S3-20	Sprint 3	User testing of the live site with 4 testers (Khadija, Gioacchino, Sohel, Chaymaa)	Khadija	Done																						
DELIVERY · GOAL: Internal buffer / final artefact readiness check																										
D-01	Delivery	Confirm GitHub artefact, slides, article progress and Moodle deadlines	Team	Done																						

Figure B2. Gantt chart by working day, 9 October to 9 November 2026, with the Scrum events of each sprint and the submission milestones.

B6 · Meeting log (Scrum events)

Date	Sprint	Event	Attendance	Outcome / decisions	Action / impediment	Status
09 Oct 2026	Sprint 1	**Kickoff / Sprint Planning**	Khadija, Alexandra, Gioacchino	QuickVolunteer chosen; product goal, roles, SDGs and Sprint 1 Goal agreed.	Set up the Scrum tracker, Gantt and meeting log.	Done
12 Oct 2026	Sprint 1	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Personas, user flow and project scope discussed.	-	Done
13 Oct 2026	Sprint 1	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Personas and journeys, prototype and ERD work distributed.	-	Done
14 Oct 2026	Sprint 1	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Prototype, normalised ERD and architecture alignment continued.	-	Done
15 Oct 2026	Sprint 1	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Prototype and schema decisions reviewed; organisations and donations removed; admin role added.	-	Done
15 Oct 2026	Sprint 1	**Sprint Review**	Khadija, Alexandra, Gioacchino	Research, personas, ERD, CASE diagrams, Flask API and prototype reviewed. Scope cut to individuals; one shared login.	Sprint 2 backlog built around one account and individuals only.	Done
15 Oct 2026	Sprint 1	**Sprint Retrospective**	Khadija, Alexandra, Gioacchino	Went well: trust, quick agreement on idea and roles, Gantt ready. To improve: workload balance; inconsistent documents.	Coordinator and helper for every item; agree shared decisions at Sprint Planning.	Done
16 Oct 2026	Sprint 2	**Sprint Planning**	Khadija, Alexandra, Gioacchino	Sprint 2 Goal confirmed (usable MVP). Work done differently by each member aligned; new goals confirmed; many things simplified.	S2-01 to S2-09 selected.	Done
16 Oct 2026	Sprint 2	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Alignment of all Sprint 1 work completed; Sprint 2 work started.	-	Done
19 Oct 2026	Sprint 2	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Database tests: 5 design problems found. Accounts active at sign-up; admins can hide reviews; each report names one target.	Update the ERD and normalisation workbook.	Done
20 Oct 2026	Sprint 2	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Progress on Sprint 2 MVP work items; no blockers recorded.	-	Done
21 Oct 2026	Sprint 2	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Progress on Sprint 2 MVP work items; no blockers recorded.	-	Done
22 Oct 2026	Sprint 2	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Integrated MVP inspected; work adapted for the final sprint day.	-	Done
22 Oct 2026	Sprint 2	**Sprint Review**	Khadija, Alexandra, Gioacchino	MVP reviewed: the core journey works end to end. Feedback: help seekers want to know who is coming.	Sprint 3 backlog: optional verification, notifications, member summary, no hours, accessibility tools moved into Sprint 3.	Done

Date	Sprint	Event	Attendance	Outcome / decisions	Action / impediment	Status
22 Oct 2026	Sprint 2	**Sprint Retrospective**	Khadija, Alexandra, Gioacchino	Went well: MVP end to end; early feedback on draft diagrams; database tests. To improve: diagrams drawn before the lecture; framework questioned mid-project.	Compare technologies during planning; bring drafts to sessions.	Done
23 Oct 2026	Sprint 3	**Sprint Planning**	Khadija, Alexandra, Gioacchino	Sprint 3 Goal agreed. Decisions: optional ID verification, in-app notifications, no hours, accessibility tools in Sprint 3, DBS out of this version.	S3 work items selected.	Done
23 Oct 2026	Sprint 3	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Sprint 3 work started: live API connection, verification and notifications.	-	Done
26 Oct 2026	Sprint 3	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Decision: members cannot edit a posted request but can close it; admins can delete but not edit (US-28).	-	Done
27 Oct 2026	Sprint 3	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Messaging kept to the back end; contact sharing and expenses recorded as known limitations. Documents aligned; final PNG and PDF files prepared for the journals and presentation.	Finish document alignment and exports.	Done
28 Oct 2026	Sprint 3	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Final checks toward the Sprint 3 Goal.	-	Done
29 Oct 2026	Sprint 3	**Daily Scrum**	Khadija, Alexandra, Gioacchino	Final inspection toward the Sprint 3 Goal.	-	Done
29 Oct 2026	Sprint 3	**Sprint Review**	Khadija, Alexandra, Gioacchino	Sprint 3 increment reviewed: accessibility tools, map and location, admin access, responsive design.	Release for the GitHub submission on 2 Nov.	Done
29 Oct 2026	Sprint 3	**Sprint Retrospective**	Khadija, Alexandra, Gioacchino	Went well: communication, listening to every idea, four areas delivered, structured testing. To improve: late database changes; documents drifting from the system.	Prepare meetings with expected issues; test with users earlier; one source of truth.	Done
Weekly / as agreed	Any	**Backlog refinement (working session)**	Khadija, Alexandra, Gioacchino	Acceptance criteria refined before each Sprint Planning.	-	Done

Table B8. Daily Scrums, Sprint Planning, Sprint Reviews and Sprint Retrospectives with attendance, decisions and actions.

B7 · Risk and issue register

ID	Type	Risk / issue	Level	Response	Owner	Status
R-01	Risk	Scope too large for three one-week sprints (organisations, donations, campaigns).	**High**	Cut to individuals only at the Sprint 1 review; later features kept as Won't (this time).	Khadija	Closed: mitigated 15 Oct
R-02	Risk	Uneven workload when work is split only by strengths.	**Medium**	Each item has a coordinator and a helper; members support each other every week.	Khadija	Open: monitored
R-03	Risk	Limited primary user evidence: the questionnaire closed with 6 responses.	**High**	Combined with national data (NCVO, DCMS) and testing with 4 users; sample size reported as a limitation.	Khadija	Closed: accepted
R-04	Issue	FastAPI taught in Week 3 after the Flask API already worked.	**Medium**	Compared both; kept Flask; wrote API_DOCUMENTATION.md.	Gioacchino	Closed: accepted
R-05	Issue	Database design allowed invalid data (in-person task without location; report with no or two targets).	**High**	CHECK constraints and Flask rules added; retested in Sprint 3.	Khadija	Closed: fixed
R-06	Issue	Database port blocked on the university network.	**Medium**	Render creates the tables on first start; MySQL hosted on Aiven.	Gioacchino	Closed: fixed
R-07	Risk	Free Render server sleeps after about 15 minutes, so the demo may load slowly in the viva.	**High**	Open the site 5 minutes before the slot; keep screenshots or a short video as backup.	Team	Open: action before viva
R-08	Risk	ID documents are lost when the free Render server restarts.	**Medium**	Admins check documents soon after upload; paid hosting in a future version.	Gioacchino	Open: accepted
R-09	Issue	Pages slow: Offer Support made 15 API calls.	**High**	Connection pool and combined calls: 15 → 5 calls (US-29).	Alexandra	Closed: fixed
R-10	Risk	Documentation drifts from the built system (diagrams, personas, test numbers).	**High**	Alignment review; diagrams, ERD and backlog updated; final check on 30 Oct.	Khadija	Open: in progress
R-11	Issue	No safe way to share an address or phone number after acceptance; messaging page not built.	**High**	Known limitation; messaging API built and tested; page planned (US-18).	Team	Open: accepted for V1
R-12	Issue	Expenses (e.g. shopping) conflict with the 'never exchange money' rule.	**Medium**	Known limitation; an expenses rule is needed before real use.	Khadija	Open: accepted for V1
R-13	Risk	Safeguarding of vulnerable help seekers during home visits.	**Medium**	Optional ID check, report a concern, suspend, member summary, area only, volunteer guide; DBS later (US-17).	Team	Open: mitigated
R-14	Risk	A team member is unavailable on the viva day.	**Medium**	Every member rehearses every section.	Khadija	Open: monitored

Table B9. Risks and issues with their level (High, Medium or Low), judged from how likely each one is and how much it would affect the project. Reviewed at each Sprint Review.

B8 · User testing and test traceability

The same four testers used the Figma prototype in Sprint 1 and the live website in Sprint 3: Khadija and Gioacchino (team), Sohel and Chaymaa (external).

ID	Stage	Finding	Change made	Story	Status
UT-01	Prototype (Sprint 1)	The entry point needed to support people who both ask for and offer help	One shared login and one account for both journeys	US-01, US-03	Done
UT-02	Prototype (Sprint 1)	Organisations and donations were broader than the micro-volunteering scope	Removed from Version 1; focus on individuals and short tasks	US-30, US-33	Done
UT-03	Prototype (Sprint 1)	Some elements had insufficient contrast	Text and interface contrast adjusted	-	Done
UT-04	Prototype (Sprint 1)	Help seekers wanted to know who is coming	Member summary shown before choosing	US-22	Done
UT-05	Live site (Sprint 3)	3/4 testers were unsure whether "filled" meant that a task was finished	Task status now reads "Volunteer accepted" or "Accepted · [name]" instead of "filled"	US-08, US-09	Done
UT-06	Live site (Sprint 3)	2/4 testers wanted to see the volunteer's verification status before applying	Verified badge shown in the member summary before a volunteer offers to help	US-22	Done
UT-07	Live site (Sprint 3)	2/4 testers had difficulty finding how to report a concern	"Report a concern about this task" link with a flag icon added to the task page	US-12	Done

Table B10. User testing findings and the changes made.

Story	MoSCoW	Automated tests	User testing	Result
US-01	Must	test_01 registration, test_02 login, test_13 suspended session blocked, test_18 'both' account, test_19 public admin sign-up blocked	UT-01	Pass
US-02	Must	test_s07 edit profile, admin notified; test_s08 profile validation; skills saved and retrieved		Pass
US-04	Must	test_04 create task; test_03, test_14 others blocked; test_71 in person needs postcode and deadline; test_72 remote has no postcode		Pass
US-05	Must	test_30-32 categories; test_s16 verified flag in list; test_s20 skills in list; test_36 cancelled task not listed		Pass
US-06	Must	test_05 apply; test_06 duplicate blocked; test_15 guest blocked; test_20 own task blocked; test_s04-s06 withdraw		Pass
US-07	Must	test_07 accept; test_11 reject; test_80-82 notifications; test_83-84 audit log		Pass
US-08	Should	test_27-29 my applications	UT-05	Pass
US-09	Should	test_21-26 my tasks; test_33-38 close a request	UT-05	Pass
US-10	Must	test_08 dual completion; test_09 duplicate blocked; test_10 not before acceptance; test_16 other user blocked; test_s03		Pass
US-11	Must	test_61-70 verification; test_s15 document only for admin, deleted after decision		Pass
US-12	Must	test_39-44 reports; test_s13 something else; test_s14 contact allowed; test_s17 suspend	UT-07	Pass
US-13	Could	test_s11 skills with optional level; test_s12 task skill importance		Pass
US-14	Could	test_s17 admin sees completed counts		Pass

Story	MoSCoW	Automated tests	User testing	Result
US-15	Could	test_54-60 reviews; test_45-49 moderation		Pass
US-16	Could	test_s11 at least one skill		Pass
US-19	Should	Manual: keyboard and every tool on all 23 pages		Pass
US-21	Must	test_78-82 notifications; test_s01-s02 offer and close notify		Pass
US-22	Must	test_s09 summary shows agreed details only; test_s10 admin summary hidden	UT-04, UT-06	Pass
US-28	Should	test_s19 admin can delete a task; test_s18 admin lists reviews		Pass
US-29	Should	Regression: all automated tests still pass after the connection pool		Pass
US-18 (API only)	Won't (this time)	test_73-77 messaging (5 tests); interface not built		Pass
Security	-	test_17 missing CSRF token rejected; test_39-40, 45-46 admin routes refused		Pass

Table B11. Test traceability. Run on 27 October 2026: 104 unique tests, 418 assertions, all passed (the unittest runner reports 320 runs because three modules re-run the 72 core tests).
